

Manajemen Komunikasi Proyek

Project Communication
Management

Agenda Hari Ini

- 1 Definisi Manajemen Komunikasi Proyek
- 2 Terminologi Manajemen Komunikasi Proyek
- 3 Proses Manajemen Komunikasi Proyek
- 4 Alat dan teknik Manajemen Komunikasi Proyek

Komunikasi

Pentingnya Manajemen Komunikasi Proyek

Project Communication Management



shutterstock.com · 1654067248

"Many experts agree that the greatest threat to the success of any project, especially IT projects, is a **failure to communicate**"

Project Communication Management



© Scott Adams, Inc./Dist. by UFS, Inc.

"Strong verbal and non-technical skills are a key factor in career advancement for IT professionals"

Apakah itu


Manajemen Komunikasi Proyek?

Communication

Definition

- Proses pertukaran informasi dua arah dari satu entitas ke entitas lain
- Manajer proyek bertanggung jawab untuk memastikan komunikasi yang tepat ke dan dari proyek
- Manajer proyek menghabiskan hampir 90% waktunya untuk komunikasi


Project



- **Project Stakeholder**
- **Management**
- **Top level management**


Komunikasi antara proyek dan pemangku kepentingan selalu dua sisi

Information Transmission

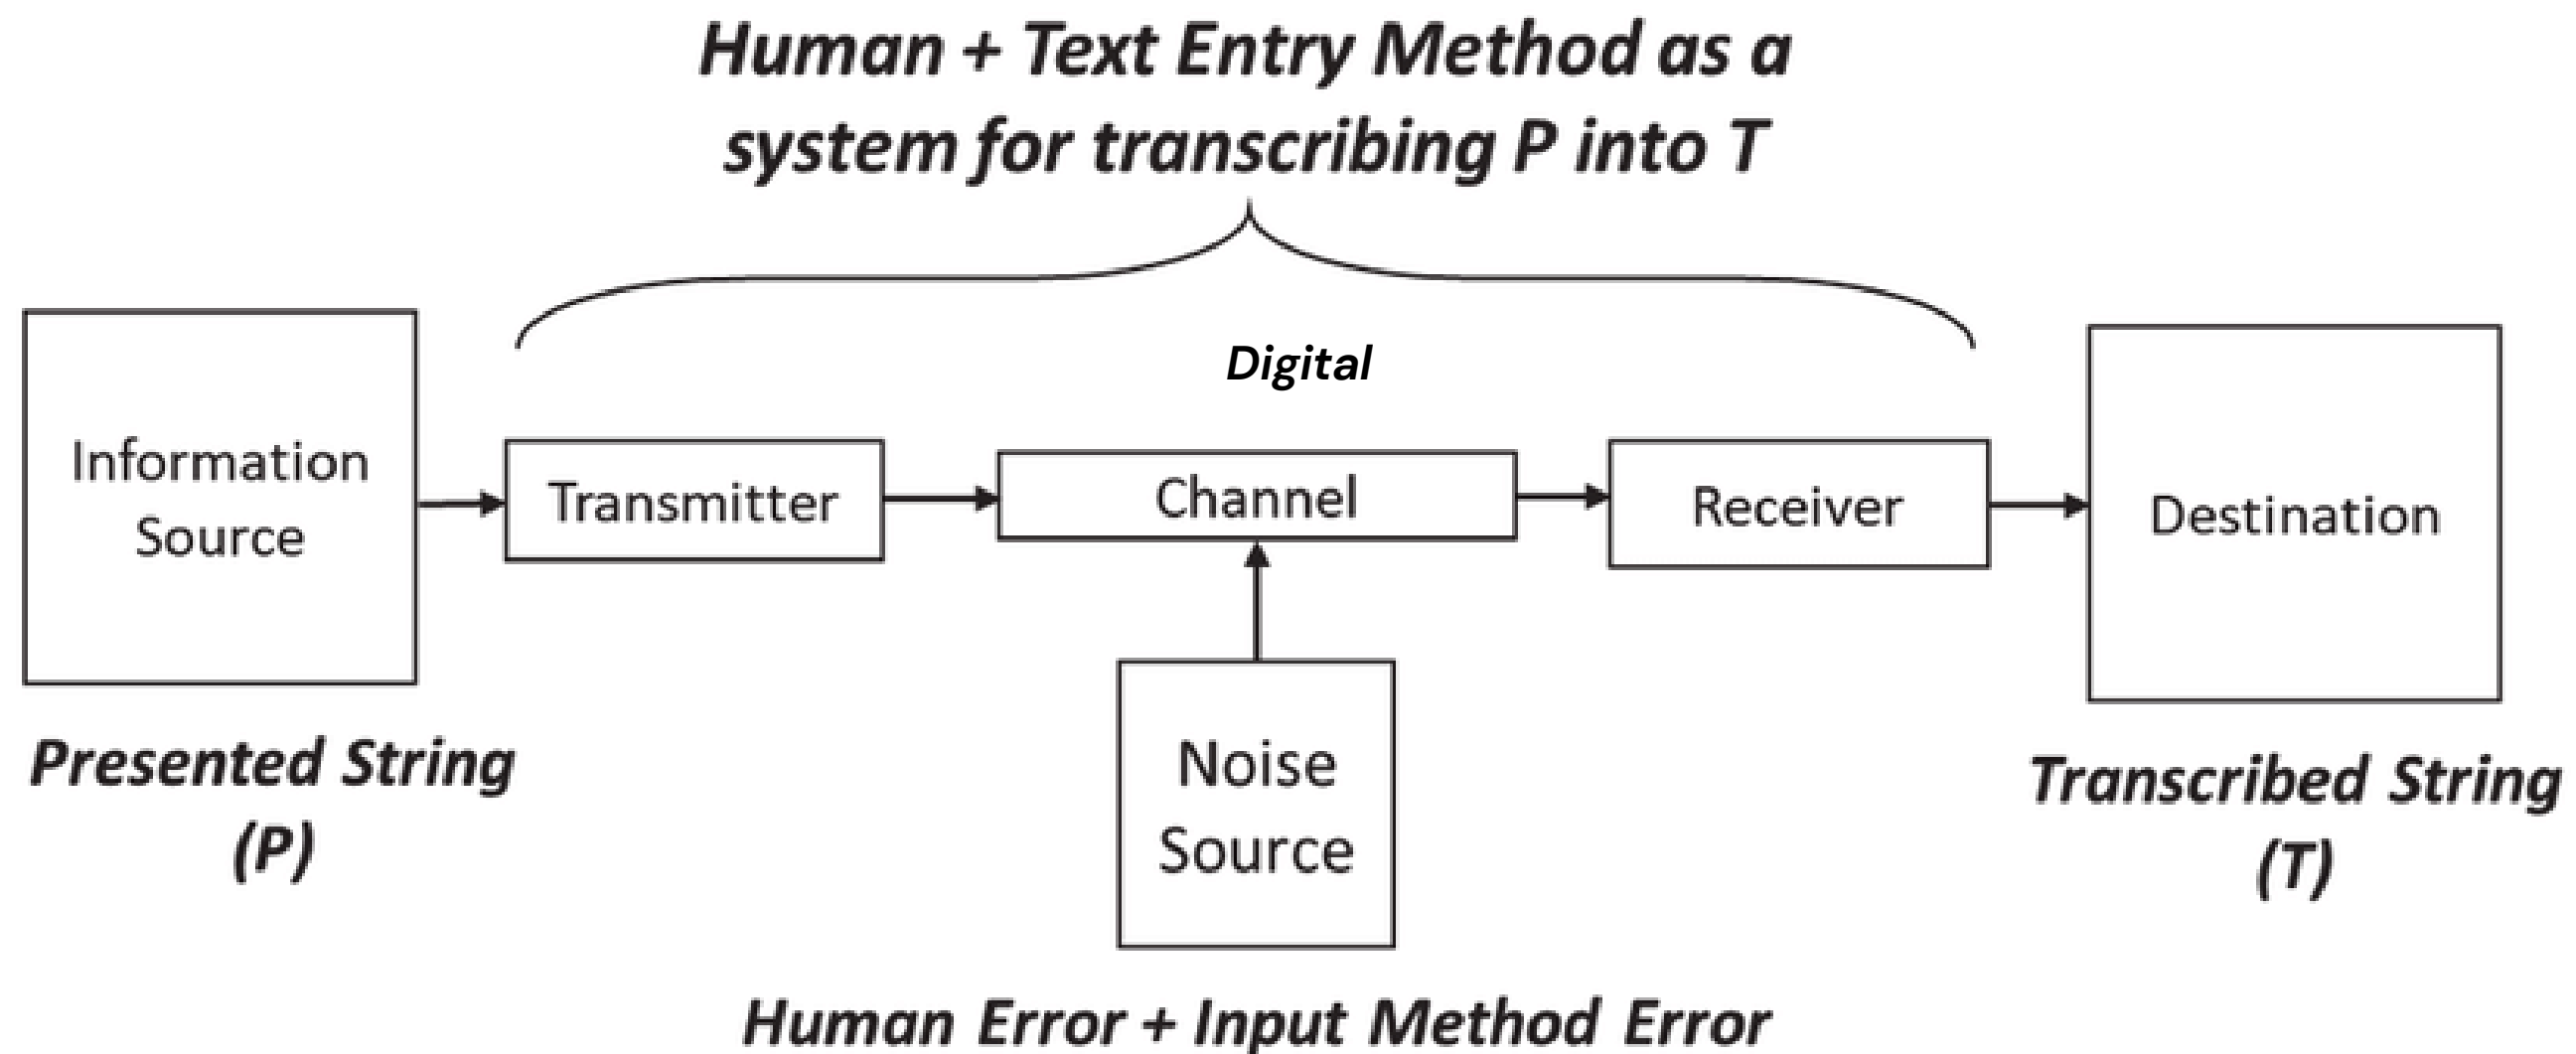

Shannon's information transmission model,

Project Communication Management

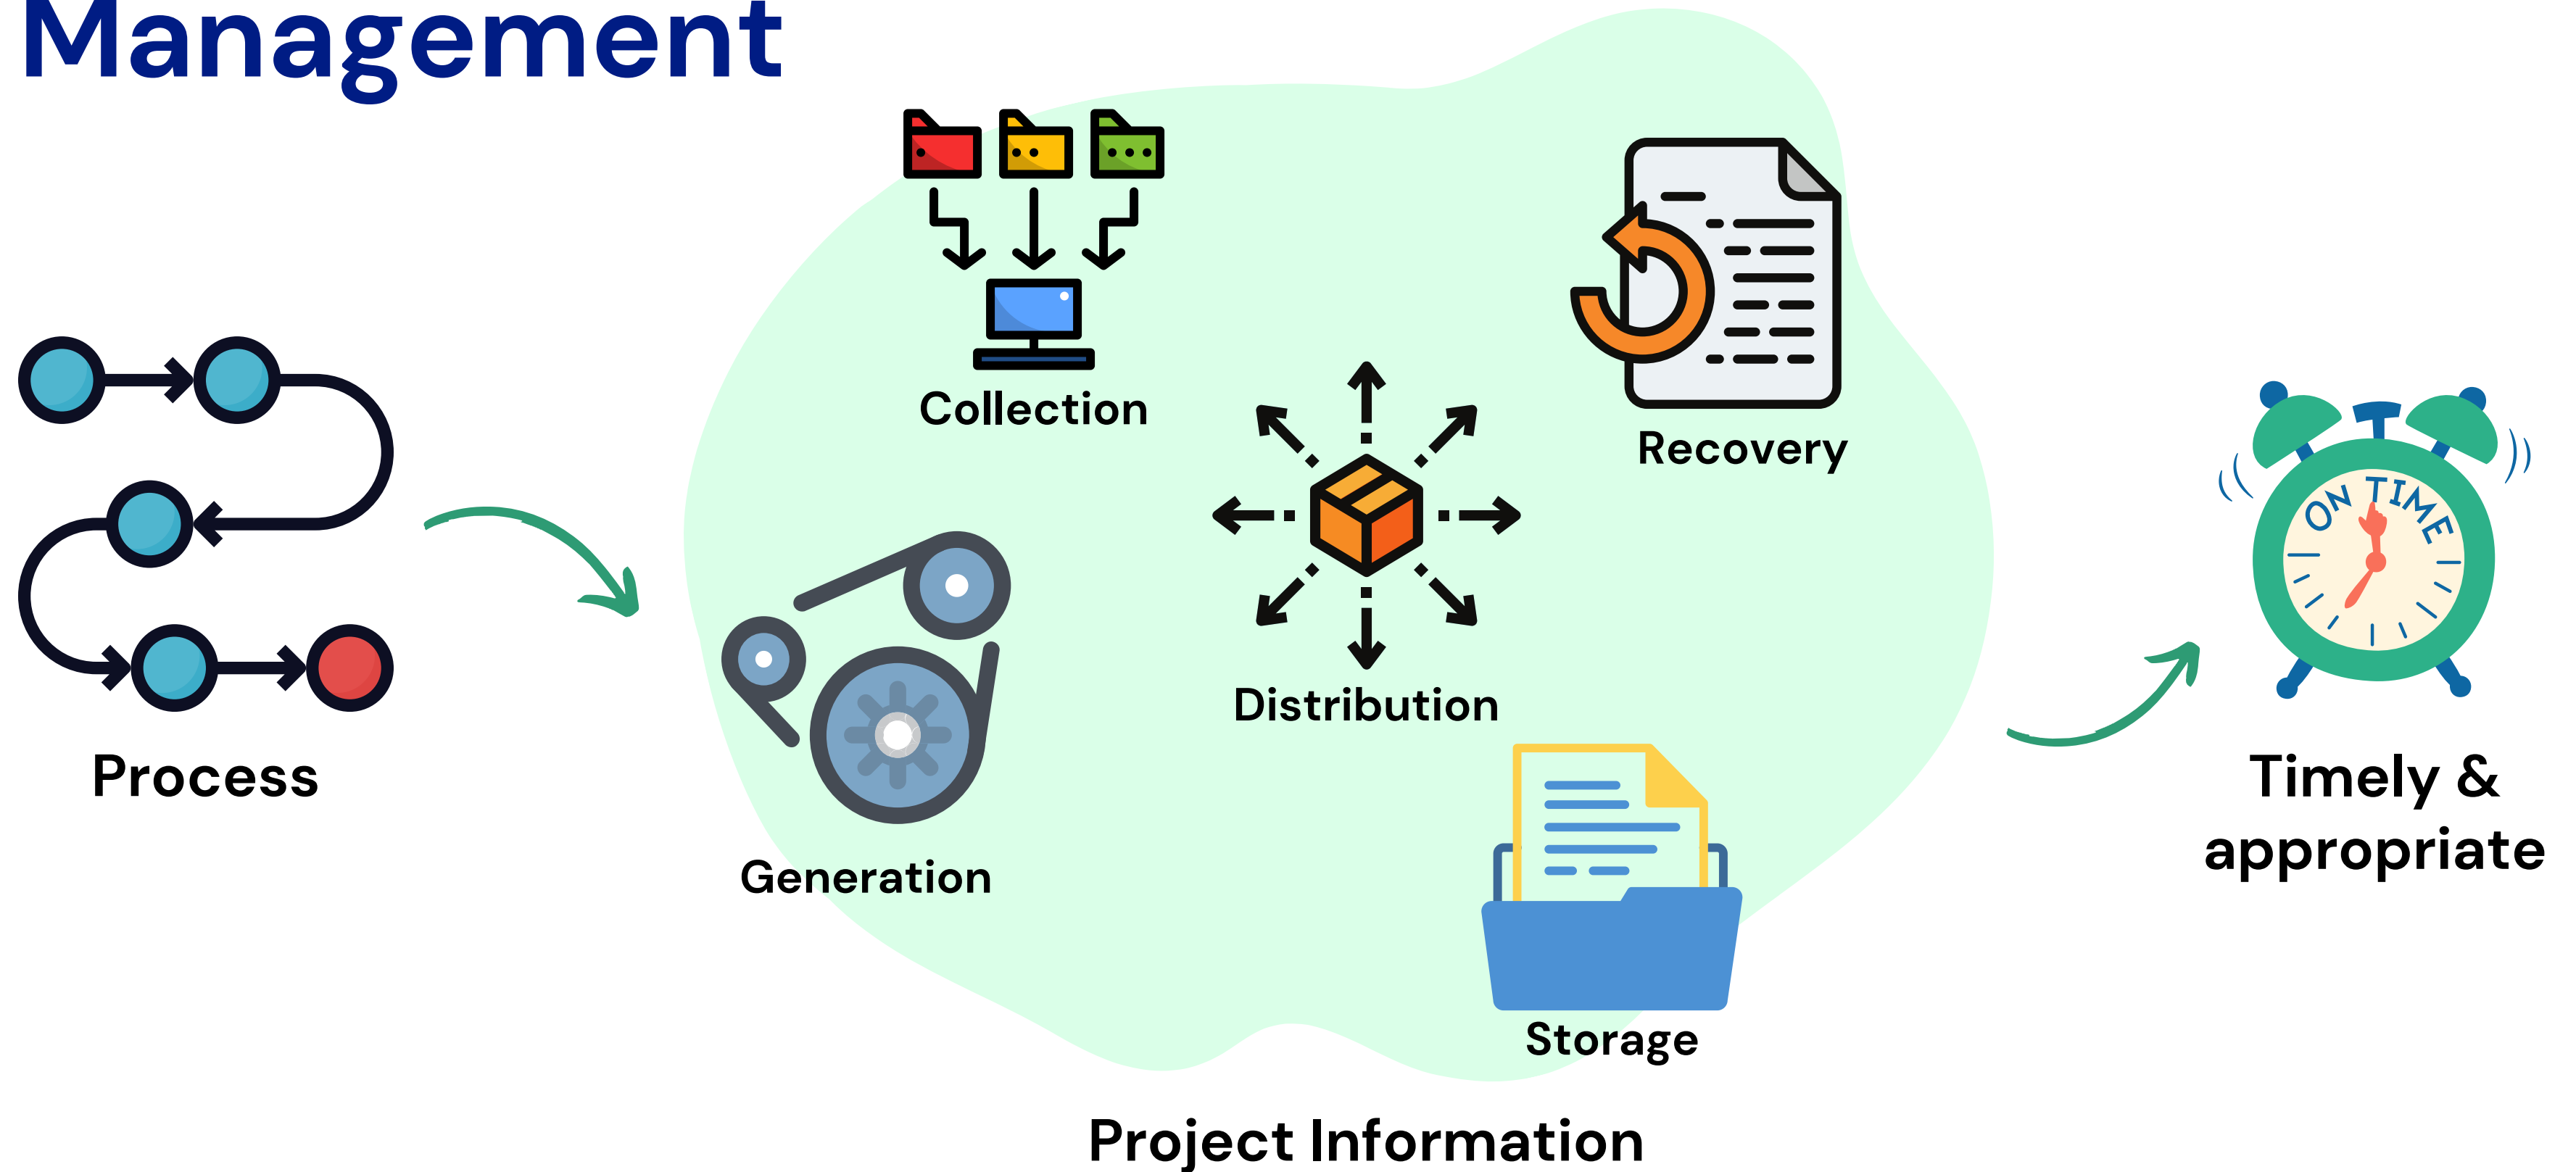

Communication Method

Komunikasi dapat dibangun secara tertulis atau verbal, dan juga formal atau informal

- 1 **Formal:** aturan tertentu harus diikuti
- 2 **Informal:** pendekatan santai
- 3 **Kombinasi:** Tertulis formal, tertulis informal, verbal formal, verbal informal

Written

- Project management plan
- Project charter
- Report

- Email
- Notes
- Group chat

Verbal

- Presentasi
- FGD

- Percakapan
- Face-to-face meeting

Formal

Informal


Communication Technology

- Mengacu pada berbagai media yang digunakan untuk komunikasi
- Popular: Virtual conference, email, telephone
- Faktor pendukung:
 - Availability
 - Project environment
 - Project Length
 - Urgency
 - Preparation Level



Communication Channel

- Media yang akan dilalui data/informasi pada proses transmisi dalam suatu sistem komunikasi
- Kompleksitas komunikasi meningkat karena ada lebih banyak saluran (channel) atau jalur di mana orang dapat berkomunikasi.
- Jumlah saluran komunikasi = $\frac{n(n-1)}{2}$

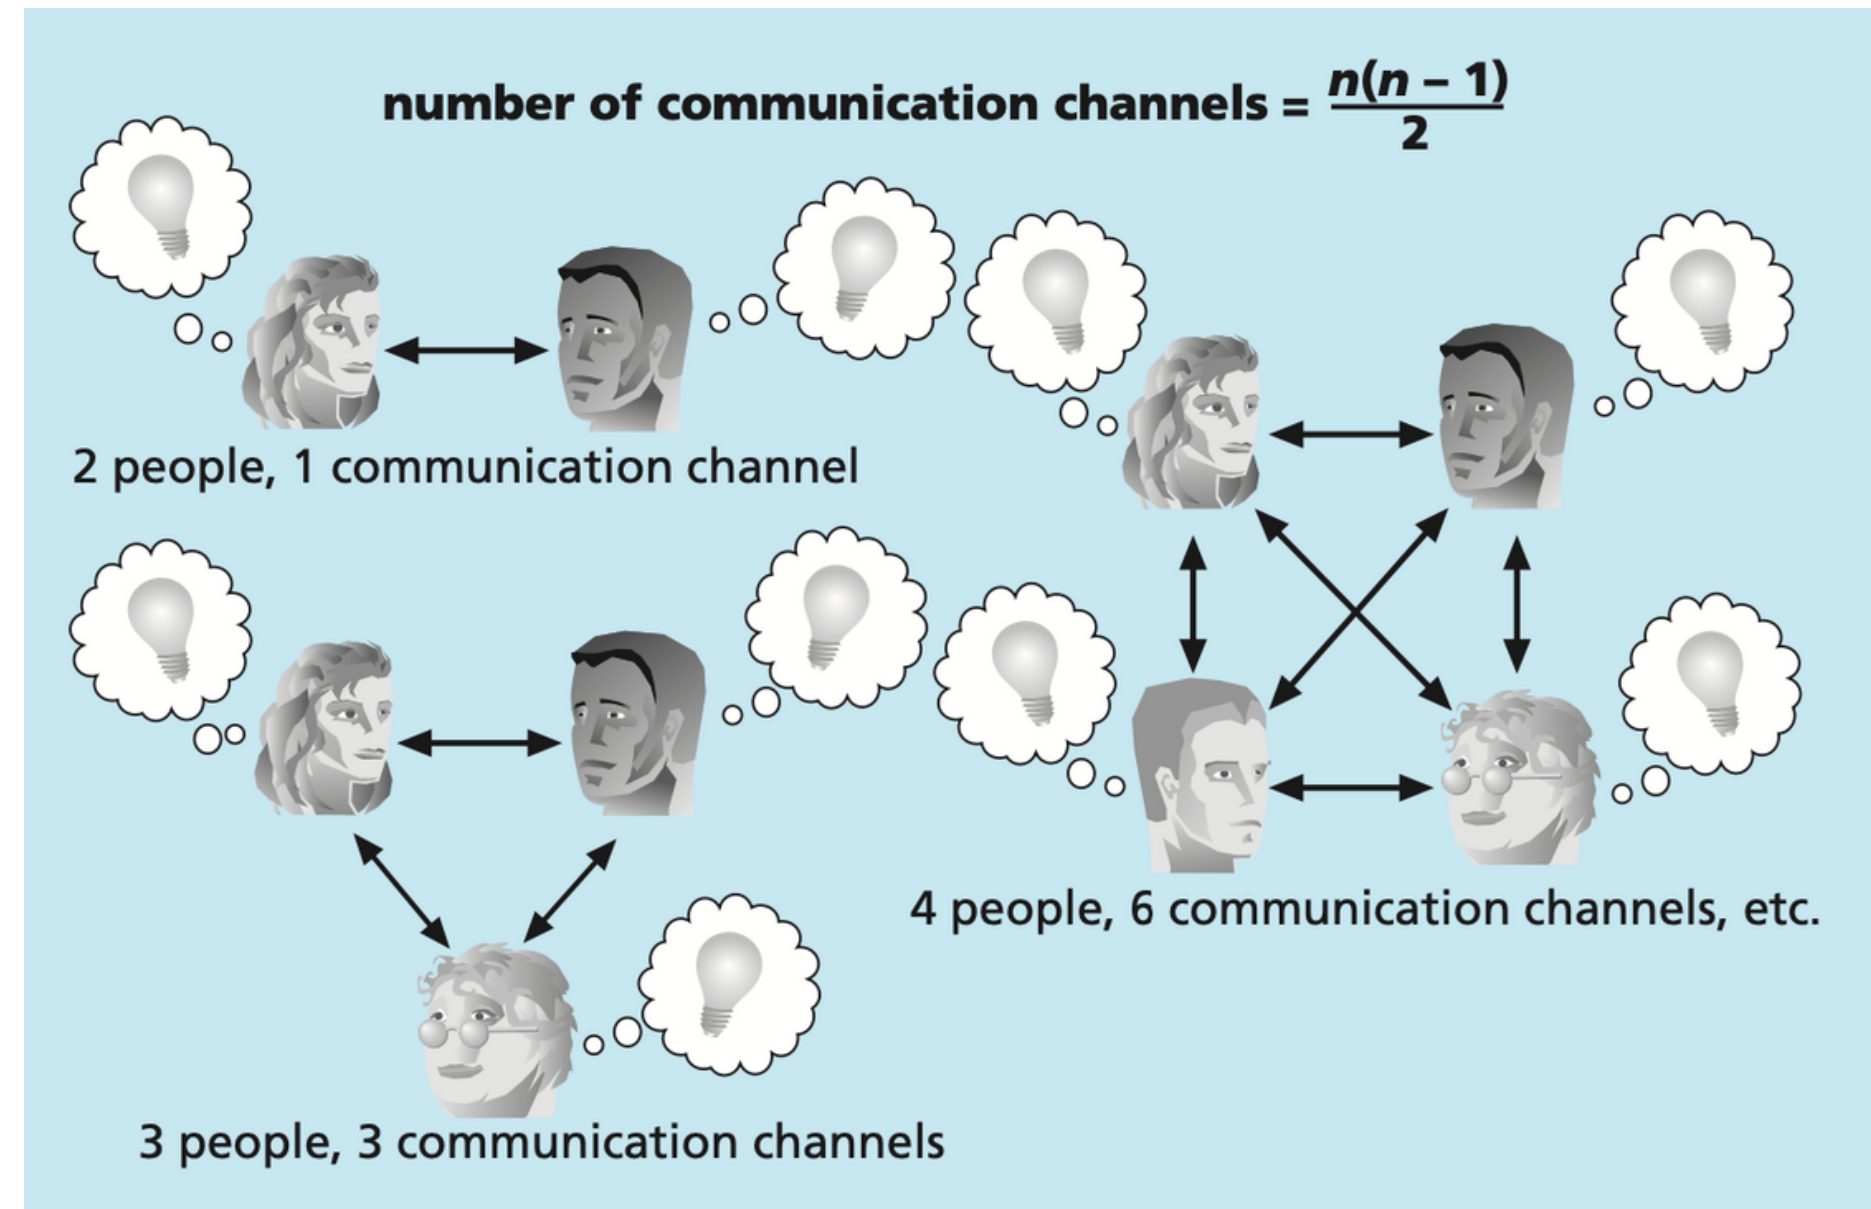

Project Communication Management

"includes the processes that are required to ensure timely and appropriate planning, collecting, creation, distribution, storage, retrieval of project information"

Project Communication Management Processes

Planning

Process: **Plan communications management**

Outputs: Communications management plan, project documents updates

Executing

Process: **Manage communications**

Outputs: Project communications, project documents updates, project management plan updates, and organizational process assets updates

Monitoring and Controlling

Process: **Control communications**

Outputs: Work performance information, change requests, project documents updates, and organizational process assets updates

Project Start

Project Finish

Project Communication Management Processes

1

Plan Communication Management

Proses pengembangan pendekatan dan rencana untuk komunikasi proyek berdasarkan kebutuhan dan persyaratan informasi stakeholder dan aset organisasi yang tersedia

Output: Dokumen Rencana Komunikasi

2

Manage Communication

Proses membuat, mengumpulkan, mendistribusikan, menyimpan, mengambil, dan disposisi akhir informasi proyek.

Output: Pembaruan rencana manajemen proyek.

3

Control Communication

Proses pemantauan dan pengendalian komunikasi di seluruh siklus hidup proyek untuk memastikan kebutuhan informasi dari stakeholder proyek terpenuhi

Output: Work performance indicator, change request, document updates.

Proses
Manajemen
Komunikasi

1. Plan Communication Management

Plan Communication Management

- Setiap proyek harus menyertakan beberapa jenis rencana manajemen komunikasi, dokumen yang memandu komunikasi proyek
- Pahami jenis informasi yang akan didistribusikan kepada stakeholder
- Melakukan analisis kebutuhan komunikasi stakeholder

Dokumen ini harus mencakup:

- 1 Persyaratan komunikasi pemangku kepentingan
- 2 Informasi: format, isi, dan tingkat detailnya
- 3 Penerima dan pengirim informasi
- 4 Metode/teknologi komunikasi
- 5 Frekuensi komunikasi
- 6 Prosedur eskalasi problem solving
- 7 Prosedur revisi untuk update dokumen
- 8 Daftar istilah umum

Stakeholder Communication Analysis

Stakeholders	Document Name	Document Format	Contact Person	Due
Customer management	Monthly status report	Hard copy and meeting	Tina Erndt, Tom Silva	First of month
Customer business staff	Monthly status report	Hard copy	Julie Grant, Sergey Cristobal	First of month
Customer technical staff	Monthly status report	E-mail	Li Chau, Nancy Michaels	First of month
Internal management	Monthly status report	Hard copy and meeting	Bob Thomson	First of month
Internal business and technical staff	Monthly status report	Intranet	Angie Liu	First of month
Training subcontractor	Training plan	Hard copy	Jonathan Kraus	November 1
Software subcontractor	Software implementation plan	E-mail	Najwa Gates	June 1

Sample Stakeholder Communication Analysis

Proses
Manajemen
Komunikasi

2. Manage Communication

Manage Communication

Menyampaikan informasi proyek kepada orang yang tepat pada waktu yang tepat dan dalam format yang berguna sama pentingnya dengan mengembangkan informasi di tempat pertama

Pertimbangan penting:

- 1 Teknologi
- 2 Metode dan media yang tepat untuk digunakan
- 3 Pelaporan kinerja

Apakah teks saja cukup atau perlu divisualkan? infografis atau video?

Apakah meeting saja cukup untuk distribusi informasi?

Apakah mengirim laporan tertulis untuk informasi proyek cukup?

Bagaimana cara distribusi informasi terbaik untuk tim virtual?



Distributing Information Through Technology

- Teknologi dapat memfasilitasi proses pembuatan dan pendistribusian informasi, bila digunakan dengan benar
- Penting untuk memilih metode dan media komunikasi yang tepat



Classifications for Communication Methods

- 1 Interactive communication**
Dua orang atau lebih berinteraksi untuk bertukar informasi melalui rapat, panggilan telepon, atau konferensi video.
- 2 Push communication**
Informasi dikirim atau didorong ke penerima tanpa permintaan melalui teknologi/alat komunikasi
- 3 Pull communication**
Informasi dikirim ke penerima atas permintaan mereka melalui teknologi/alat komunikasi

Communication Media

- Penting untuk mempertimbangkan media mana yang akan digunakan sesuai dengan karakteristik informasi
- Media dapat berupa:
 - Hard copy
 - Phone call
 - Voice mail
 - E-mail
 - Meeting
 - Website

Key: 1 = Excellent, 2 = Adequate, 3 = Inappropriate						
How Well Medium Is Suited to:	Hard Copy	Phone Call	Voice Mail	E-mail	Meeting	Website
Assessing commitment	3	2	3	3	1	3
Building consensus	3	2	3	3	1	3
Mediating a conflict	3	2	3	3	1	3
Resolving a misunderstanding	3	1	3	3	2	3
Addressing negative behavior	3	2	3	2	1	3
Expressing support or appreciation	1	2	2	1	2	3
Encouraging creative thinking	2	3	3	1	3	3
Making an ironic statement	3	2	2	3	1	3
Conveying a reference document	1	3	3	3	3	2
Reinforcing one's authority	1	2	3	3	1	1
Providing a permanent record	1	3	3	1	3	3
Maintaining confidentiality	2	1	2	3	1	3
Conveying simple information	3	1	1	1	2	3
Asking an informational question	3	1	1	1	3	3
Making a simple request	3	1	1	1	3	3
Giving complex instructions	3	3	2	2	1	2
Addressing many people	2	3 or 1*	2	2	3	1

*Depends on system functionality

Source: Tess Galati, *Email Composition and Communication (EmC2)*, Practical Communications, Inc., www.pracom.com (2001)

Reporting Performance

- **Status reports:** menjelaskan di mana proyek berdiri pada titik waktu tertentu
- **Progress reports:** menggambarkan apa yang telah dicapai tim proyek selama periode waktu tertentu
- **Forecasts:** Perkiraan memprediksi status dan kemajuan proyek di masa depan berdasarkan informasi dan tren masa lalu

TABLE 3-14 Sample weekly progress report

Project Name: Project Management Intranet Project
Team Member Name: Cindy Dawson, cindy_dawson@jwdconsulting.com
Date: August 5
Work completed this week: –Worked with Kevin to start the intranet site construction –Organized all the content files –Started developing a file naming scheme for content files –Continued work on Ask the Expert and User Requests features –Met with preferred supplier –Verified that their software would meet our needs –Discovered the need for some customization
Work to complete next week: –Continue work on intranet site construction –Prepare draft contract for preferred supplier –Develop new cost estimate for outsourced work
What’s going well and why: The intranet site construction started well. The design was very clear and everyone knows what he’s doing.
What’s not going well and why: It is difficult to decide how to organize the templates and examples. Need more input from consultants and clients.

Sample Weekly Progress Report

Proses
Manajemen
Komunikasi

3. Control Communication

Control Communication

"Memastikan aliran informasi yang optimal di seluruh siklus hidup proyek"



Tools & Techniques:

- 1 Reporting systems
- 2 Expert judgment
- 3 Meetings
- 4 External facilitator



Suggestion for Communication

Komunikasi yang baik sangat penting untuk manajemen dan keberhasilan proyek TI.

- 1 Developing Better Communication Skills
- 2 Running Effective Meetings
- 3 Using Collaborative Tools Effectively
- 4 Gunakan template untuk komunikasi proyek

Developing Better Communication Skills

- Pelatihan keterampilan komunikasi: kegiatan bermain peran
- Meningkatkan komunikasi dengan orang-orang dari berbagai negara dan budaya
- Belajar berpartisipasi dalam pertemuan virtual dan panggilan konferensi.
- Dibutuhkan kepemimpinan untuk meningkatkan komunikasi



Running Effective Meetings

Apakah pertemuan
dapat dihindari?

1

Apa tujuan dan hasil yang
diharapkan dari pertemuan?

2

Siapa yang harus hadir?

3

Sediakan agenda
sebelum rapat

4



5

Siapkan handouts dan alat
bantu visual

6

Jalankan meeting dengan
profesional

7

Apa aturan dasar untuk
rapat?

8

Jalin hubungan baik

Using Collaborative Tools Effectively

- Media kolaboratif sesuai dengan kebutuhan
- Mengirim ke orang yang tepat
- Subyek dan body email yang jelas
- Berikan otorisasi berbagi dan mengedit yang tepat



Using Templates for Project Communications

- Memberikan contoh dan template untuk komunikasi proyek menghemat waktu dan biaya
- Penelitian menunjukkan bahwa perusahaan yang unggul dalam manajemen proyek memanfaatkan template secara efektif

Project X Description


Objective: Describe the objective of the project in one or two sentences. Focus on the business benefits of doing the project.

Scope: Briefly describe the scope of the project. What business functions are involved, and what are the main products the project will produce?

Assumptions: Summarize the most critical assumptions for the project.

Cost: Provide the total estimated cost of the project. If desired, list the total cost each year.

Schedule: Provide summary information from the project’s Gantt chart, as shown. Focus on summary tasks and milestones.

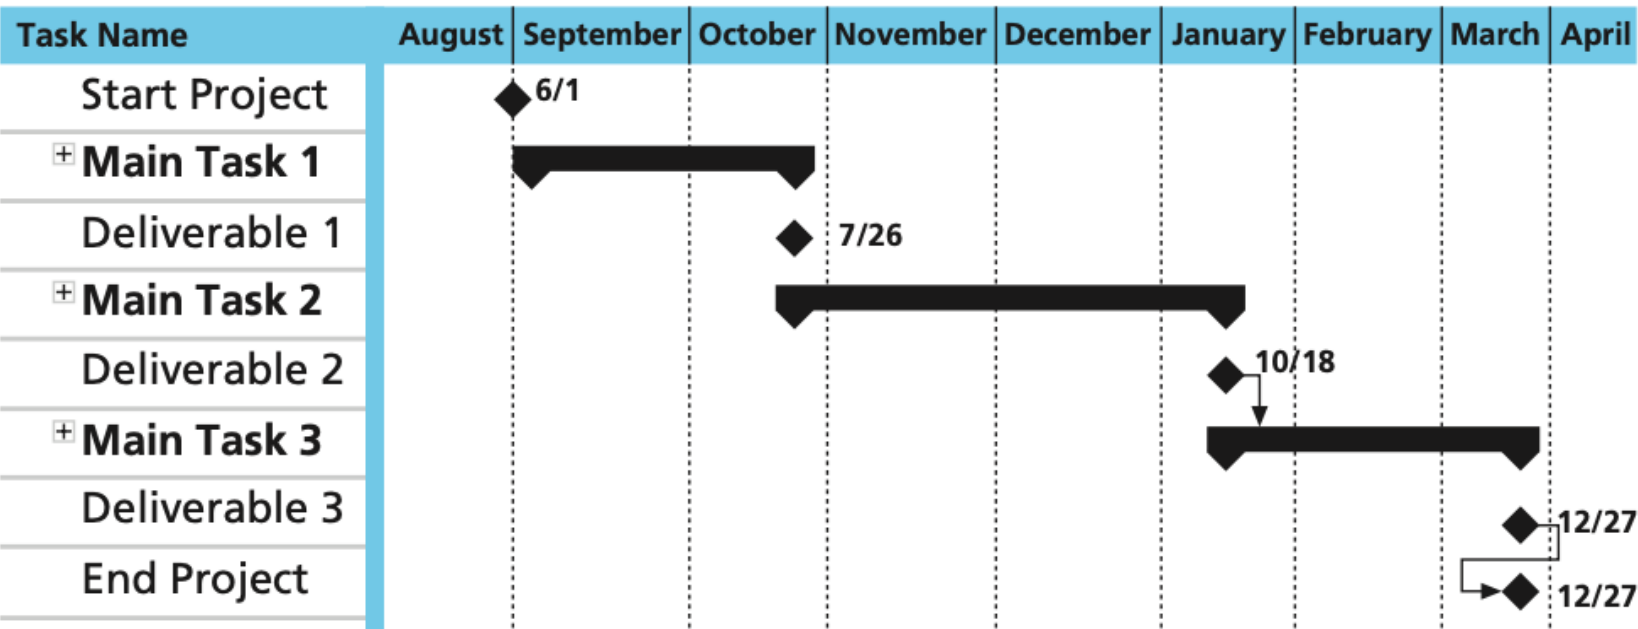

© Cengage Learning 2016

FIGURE 10-4 Sample template for a project description

Sample Templates for Monthly Progress

I. Accomplishments for January (or appropriate month):

- Describe most important accomplishments. Relate them to project's Gantt chart.
- Describe other important accomplishments, one bullet for each. If any issues were resolved from the previous month, list them as accomplishments.

II. Plans for February (or following month):

- Describe most important items to accomplish in the next month. Again, relate them to project's Gantt chart.
- Describe other important items to accomplish, one bullet for each.

III. Issues: Briefly list important issues that surfaced or are still important. Managers hate surprises and want to help the project succeed, so be sure to list issues.

IV. Project Changes (Dates and Description): List any approved or requested changes to the project. Include the date of the change and a brief description.

Final Project Documentation Items

- | | |
|-------|---|
| I. | Project description |
| II. | Project proposal and backup data (request for proposal, statement of work, proposal correspondence, and so on) |
| III. | Original and revised contract information and client acceptance documents |
| IV. | Original and revised project plans and schedules (WBS, Gantt charts and network diagrams, cost estimates, communications management plan, etc.) |
| V. | Design documents |
| VI. | Final project report |
| VII. | Deliverables, as appropriate |
| VIII. | Audit reports |
| IX. | Lessons-learned reports |
| X. | Copies of all status reports, meeting minutes, change notices, and other written and electronic communications |

Lesson Learned Report

PROJECT LESSONS-LEARNED REPORT

Total length of report: 2-3 pages.

Please refer to the [Deliverable Description](#) for more information on the purpose and use of this report

Project Title:	
Country:	
Related CPAP Outcome	
Project Description and Key Lessons-Learned	
Brief description of context	Please give a brief description of the country context. ○ What were the main challenges being faced at the start of the project?
Brief description of project	A short description of the project should be provided here. ○ What were the issues the project tried to address? ○ What solutions the project tried to offer? What were its major outputs?
Key project successes	Please describe what has worked well. ○ What have been the key successes of this project? ○ What factors supported this success?

Software to Assist Project Communication

The logo for Monday.com, featuring three slanted parallel bars in red, yellow, and green, followed by the text "monday.com".The logo for ClickUp, featuring a colorful geometric icon of four triangles forming a square, followed by the text "ClickUp".The logo for smartsheet, featuring a grey document icon with a blue checkmark, followed by the text "smartsheet".The logo for Hive, featuring three horizontal orange bars, followed by the text "Hive".The logo for Forecast, featuring a purple hexagon with a white stylized 'F', followed by the text "Forecast".The logo for wrike, featuring a green checkmark icon, followed by the text "wrike".The logo for clarizen, featuring the text "clarizen" in a blue sans-serif font.The logo for celoxis, featuring a blue circular icon with a white swirl, followed by the text "celoxis".The logo for FunctionFox, featuring a light blue icon of an open book or folder, followed by the text "FunctionFox".The logo for GANTT PRO, featuring the text "GANTT PRO" in a bold, green, blocky sans-serif font.The logo for awork, featuring the text "awork" in a blue sans-serif font, with a small robot head icon replacing the 'o'.The logo for meister task, featuring a blue circular icon with a white checkmark, followed by the text "meister task".The logo for ProWorkflow, featuring an orange gear icon, followed by the text "ProWorkflow".The logo for Zoho Projects, featuring the word "ZOHOPROJECTS" in a colorful, blocky font where each letter is a different color.The logo for nutcache, featuring a teal circular icon with a white swirl, followed by the text "nutcache".

Terima kasih

Semoga hari
Anda luar biasa.
